Earned Value Cost Report

Website redesign | Currency: PKR | Generated 2026-10-26

Schedule: behind plan (SPI 0.85) Cost: over budget (CPI 0.70) Planned 64.2% vs actual 54.5% complete

1. Project status

Metric	Formula	Value	Good sign
Budget at Completion (BAC)	Total budget	PKR 105,000	
Planned Value (PV)	Planned % x BAC	PKR 67,400	
Earned Value (EV)	Actual % x BAC	PKR 57,200	
Actual Cost (AC)	Time and expense records	PKR 82,300	
Schedule Variance (SV)	EV - PV	-10,200	Positive
Schedule Perf. Index (SPI)	EV / PV	0.85	Above 1
Cost Variance (CV)	EV - AC	-25,100	Positive
Cost Perf. Index (CPI)	EV / AC	0.70	Above 1
Cost variance %	CV / EV x 100	-43.9%	Positive

2. Forecast

Method	ETC	EAC	VAC (BAC - EAC)
EAC (one-time overrun)	47,800	130,100	-25,100
EAC (present CPI) (selected)	68,775	151,075	-46,075
EAC (CPI and SPI)	81,039	163,339	-58,339
EAC (80/20 weighting)	65,863	148,163	-43,163
EAC (80/20, as printed on slide)	506,495	588,795	-483,795
EAC (new estimate)	n/a	n/a	n/a

TCPI to meet original budget: 2.11 | TCPI to meet revised budget (selected EAC): 0.70 | Total EMV of risks: PKR 7,800

TCPI above 1 means the team must work more efficiently than it has so far.

3. Cost comparison

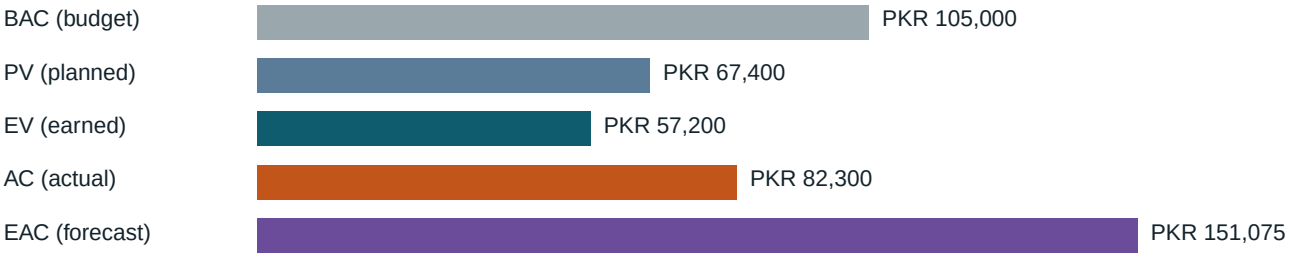

4. Tasks

Task	BAC	PV	EV	AC	CV	CPI	SPI
Requirements	8,000	8,000	8,000	8,400	-400	0.95	1.00
UI/UX design	15,000	15,000	14,250	16,500	-2,250	0.86	0.95
Frontend build	30,000	21,000	18,000	24,000	-6,000	0.75	0.86
Backend and API	35,000	21,000	15,750	31,000	-15,250	0.51	0.75
Testing and QA	12,000	2,400	1,200	2,400	-1,200	0.50	0.50
Deployment	5,000	0	0	0	0	n/a	n/a

5. AI cost analysis

Severity	Task	Finding
high	UI/UX design	Budget exhausted early: Actual cost already exceeds the whole budget while only 95%…
high	Frontend build	Severe cost overrun: CPI 0.75: each unit of value costs about 1.33 units.
high	Backend and API	Severe cost overrun: CPI 0.51: each unit of value costs about 1.97 units.
high	Testing and QA	Severe cost overrun: CPI 0.50: each unit of value costs about 2.00 units.
medium	UI/UX design	Cost overrun: CPI 0.86 is below 0.90.
medium	Backend and API	Well behind schedule: SPI 0.75: only 75% of the planned value has been earned.
medium	Testing and QA	Well behind schedule: SPI 0.50: only 50% of the planned value has been earned.
low	Frontend build	Behind schedule: SPI 0.86.

Generated by an automated analysis. Review flagged items against source records before acting on them.
